

WEEKLY PROJECT SUMMARY



Houston Engineering, Inc.
1401 21st Avenue North
Fargo, ND 58102
Ph. (701) 237-5065

Week Ending: 3/4/18

Project: Fish Lake Dam Modification

Project No.: 8513-001

Contractor: Hough Construction.
Sub:

Weather Summary This Week: Mild. Highs ranged from mid-30's to upper-30's. Lows ranged from single digits to mid-teens.

Work Completed This Week:

Monday – Channel excavation and rock placement

Tuesday – Channel excavation and built west berm.

Wednesday – Started east berm and cutting concrete dam to elevation.

Thursday – Finished cutting concrete dam to elevation and started placing top layer of rock (class 3 riprap).

Friday – No construction activity. Hauled boulders on-site.

Saturday – No construction activity.

Sunday – No construction activity.

Weather Delays (Days lost to weather): None.

Challenges and Solutions:

- None

Projected Work Schedule for Next Week: Start installing weirs and continue placing class 3 riprap

Additional Comments: None

Resident Project Representative: Mike Buerkley, 701-371-9866

Date: 3/5/18

WEEKLY PROJECT SUMMARY



Excavating channel, west side.



West berm built, starting east berm.



Cutting dam to elevation.


WEEKLY PROJECT SUMMARY



Dam to elevation, starting rock placement.



Tuesday

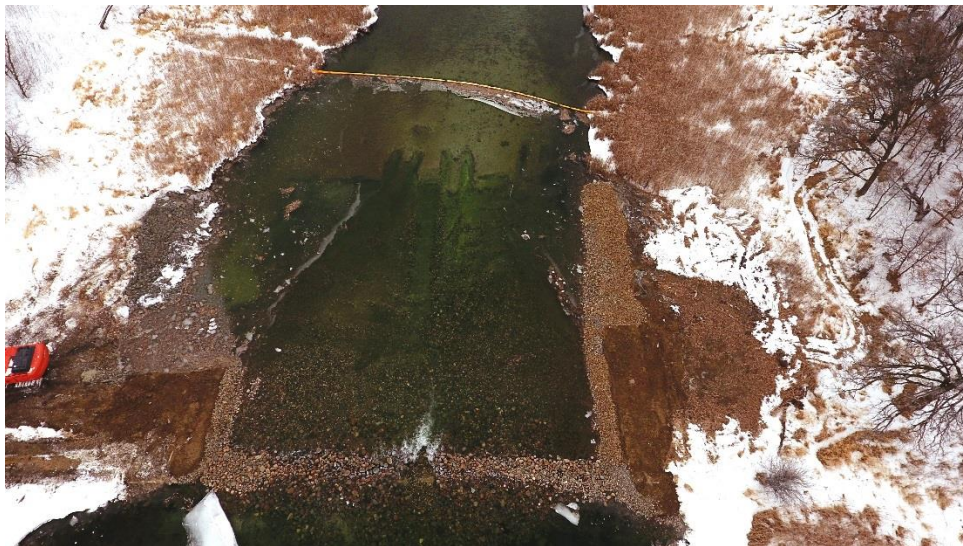

Dam to elevation (Friday).
